FOR MYSORE STATE

1-1-62.

Pub(RD)IV (195 4) Department.

Ms SERIES.

G.O. NO. 2316 F

Dated 26-11-54.

Passed

Supdt

[Despatch Abstract.]

C.Bs - S. Kanara Project Area — Block I — construction of a Primary Health centre at Bajpe — Additional expenditure — Sanctioned.

B. S. Bhasker Rai,
B.A., LL.B.,
ADVOCATE
VICE-CHAIRMAN
MUNICIPAL COUNCIL

~~Phone—882~~
OFFICE:
II FLOOR
DIAMOND BUILDINGS
HAMPANKATTA, MANGALORE-1

Date 12th June '54 195

To,

The Director Of Community
Projects, MADRAS.

-8130!

Sub:- Primary Health Centre, Bajpe -
Deepening of the Well - Full grant
prayed from the Community funds.

Sir,

On behalf of the beneficiaries of Bajpe , Sri. John Fernandez has taken up the work of the Bajpe Primary Health Centre. The building is practically complete except for the fixing up of the bolts and nets & painting. It would be ready for occupation by the end of this month.

Along with that, the Committee had taken up the work of digging the Well up to 42 feet, but as we did not strike water we have gone 15 feet deeper at the request of the officials concerned. We had agreed to pay 1/2 the cost up to 42 feet only, beyond that it is not possible as we have stopped further collection in view of the depression in the financial position of the people. So far we have invested some money out of our building collection to deepen the Well beyond 42 feet. This money is needed to complete the Hospital building. We therefore request you to take the deepening and construction of ~~necessary~~ Wall beyond 42 feet on full grant basis.

Yours

Otherwise we have to stop all further work including that of the Hospital building also. Hence please sanction necessary full grant to the Well work beyond 42 feet and oblige. Please treat this as urgent.

Thanking you.

Yours Ever,

B. Baradi Rai

Govt. Of Madras,
Agri(D V) Deptt.

Pl. agree.
23/6.

Endt No. 81308 D V/54-1 dt. 23.6.54.

Communicated to the Project Executive officer, Mangalore for ~~disposal~~ remarks

Accounts & Special officer
Agri(D V) deptt.

22/6/54 22/6/54.

To
The Project Executive officer,
Mangalore,
South Kanara dist
(R D Thumth)

Ref.C.No.203/[illegible] Project Executive Office,S.I.,
Mangalore, dated 18-7-1954.

From
Sri.N.Ramesh[illegible]
Project Execut[illegible]
Mangalore.

To The Director of Community Projects
& Ex.Officio Addl. Secretary to
Government, Madras.

Sub: Community Projects--South Kanara--Primary Health Centre--Bajpe--Construction of a well--Deepening beyond the sanctioned depth--Extra Cost--Full payment.

Ref: Govt.Endt. No.[illegible] P.1/54-1 (Agri.Dept.) dated 28-6-54.

---

2 ans

Sri.K.D.Bhasker Rai, a member of the Hospital Building Committee, Bajpe asks for the full payment of the cost involved in the further deepening of the well attached to the Hospital, beyond the depth provided in the sanctioned estimate relating the well. The well estimate for Rs.640/- was included in the main Hospital estimate sanctioned in G.O.Ms. No.1466 P.H. dated 27-5-1952 for a total sum of Rs.27,300/-, out of which 50% i.e. Rs.12650/- is payable from Community Project funds. The sanctioned depth of the well is 40 ft. (though sinking has been provided upto 42 ft. in the estimate, perhaps by mistake). As water could not be tapped at this depth, further deepening of the well by 18 ft. or till water was tapped was approved in Govt.Memo No.37627 Pub.(C.F.Audit)/52-2, dated 22-10-1952. But the deepening had to be done upto 58 ft. when a rocky outcrop was seen with a depth of 3' ft. of water at the height of summer (May 1954). The Asst. Engineer (C.F.) reports that based on the quantities of materials required for completion of the present well, the cost comes to Rs.6700/-. A copy of his report together with a comparative statement of differences in the prescribed form is enclosed. According to the Asst. Engineer's report, the net excess amount required against the original estimate is Rs.2140/-.

2. Normally, in such cases where there is deviation from the original estimate involving extra work with consequent extra cost, the beneficiary agrees to the payment of the expenditure in the same proportion as agreed to in respect of the original estimate. But in this singular instance, Sri.Bhasker Rai who is not the beneficiary who has executed the agreement, but only a member of the Building committee, has chosen to ask for full payment for the extra work done in sinking the well, apparently on behalf of Sri.John Fernandez who has taken up the work of the Bajpe Primary Health Centre at half rates and executed the agreement as a beneficiary. On a reference made by me on 25-6-54, the President of the Building Committee wrote to me on 30-6-54 that the Committee had not authorised anyone to hold correspondence on its behalf till then and that when such authorisati was given, the fact would be duly intimated to this office. Subsequently, however, it is learnt that the Building Committee has authorised Sri.Bhasker Rai to carry on correspondence on its behalf and also approved of his action till then. Evidently, Sri.Bhasker Rai, in order to strengthen his position, prevailed upon the Committee to pass such a resolution, explaining to the Committee that the letter addressed by him to the Government was intended to get more money from the Government for the work undertaken on behalf of the Committee.

3. I, however, wanted to know the mind of the Committee and also the beneficiary Sri.J.Fernandez and wrote to the President to convene a Committee meeting today at 3 P.M. when I would also be present to consider the question of payment for the well and also the question of proceeding with the other items of work provided

P.T.O.

in the sanctioned estimate viz. 1. putting up of a sentic tank etc. and (2) forming approaches and inside the compound and fixing a gate for each of which items, a lump sum of Rs.1500/- has been provided. The Asst. Engineer and the Asst.Project Officer were also asked to be present. But today, when I went to Anjar, none of the Committee members turned up and the President was said to be laid up with fever. It was learnt that the President had orally informed some of the members about the proposed meeting and many of them were absent from the village. I understand that there is a split among the members due to the unsatisfactory conduct of Sri.Bhasker Rai and Sri.Fernandez in connection with the work of construction of the Hospital building and also in regard to collection of contributions. The President is more or less a figure head - a non-entity in the eyes of some of the members including Sri.Bhasker Rai and Sri. Fernandez. I could not therefore ascertain the views of the members of the Committee on the application of Sri.Bhasker Rai under report.

4. In any case, I feel that the Committee will only favour the demand for full payment for the extra work done in regard to the construction of the well as it is a demand for getting more money from the Govt. In fact, the beneficiary Sri.Fernandes seems to be hard up for money to complete the work undertaken by him and is complaining against some members of the public that they have not paid the promised amounts and against the Government that he has not been paid his dues, although, he has been shown the maximum concession possible consistent with rules in paying part bills for the work done. It is therefore futile to expect the Committee to agree to the payment of 50% of the extra expenditure involved.

5. I therefore recommend that sanction may be accorded for full payment in respect of the work done in excess of the work agreed to be done at half rates according to the sanctioned estimate, and that an additional sum of Rs.2140/- may be sanctioned as reported by the Asst. Engineer. The total amount for the entire work of the hospital will come to Rs.15700/- as against the provision of Rs.15000/- in the overall programme. The excess sum of Rs.570/- may possibly be found in the savings under other items included under 'Health and Rural Sanitation.'

6. In this connection, I have also to submit that Sri.Fernandez has already declined to carry out the remaining 2 items of work, for each of which a lump sum of Rs.1500/- has been provided in the estimate, at half rates on the ground that these items have not been specifically mentioned in the agreement. The Asst. Engineer has, after working out the details, estimated the actual cost of these items at Rs.900/- and Rs.1000/- respectively, making a total of Rs.1900/- as against the sanctioned amount of Rs.3000/-. I have called the Committee meeting again on 25-7-1954 at 3 P.M. to consider this question and issued notices to all the members to attend the meeting. A further report will be sent in this matter by 26-7-1954.

Yours faithfully,

21.7.54

Project Executive Officer.

JC/21-7-54.

Copy of letter No.538-T dated 1-7-1954 from the Asst. Engineer, Mangalore, to the Project Executive Officer, Mangalore

Sub: Community Projects--South Kanara--Primary Health Centre at Kaipe--Revised Estimate for the well.

Ref: 1.Sri.Bhasker Rai's letter dated 12-6-1954.
2.Ref.C.No.69/52-T.

A well estimate costing Rs.4100/- included in the main hospital estimate for Kaipe had been sanctioned in G.O.Ms.No.1466 dated 27-6-1952. In the original estimate, the depth of the proposed 10'-0" diameter well had been 40 ft. As there was no trace of water at this depth, the matter was referred to the Govt. in the Project Executive Officer's No.1286/53-A dated 7-10-1953 for increasing the depth by another 10 ft. or till water is traced.

In the Govt. Memo No.37027 Sub.(2)P.Audit)/53-3 dated 22-12-1953, the proposal for deepening the well further by 10 ft.or till water is traced has been approved. But a good supply of water could be had only after the depth of 57 ft. and at this depth nearly sufficient water was met with for the month of May 1954. Based on the quantities of materials required for completing the present well, a revised estimate for the prepared costing Rs.7700/-.

The cost of this well excluding the water supervision and establishment charges and unforseen items of works is Rs.6925/-. The provision in the original sanctioned estimate excluding the water supervision charges and unforseen items of works is Rs.4485/-.

The excess now required against the original estimate is Rs.6925 minus Rs.4485 i.e. Rs.2440/-.

A comparative statement for the above work is enclosed for reference and for necessary further action.

ESTIMATE FORM.—Comparative Statement of Differences. P.W.D. V-18 (inner)—46,406—20-6-52

Description of work.	Item No.	Original estimate. Quantity.	Rate.	Amount.	Revised estimate. Quantity.	Rate.	Amount.	More.	Less.	Explanation of difference.
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)
Constructing wood wrought and put up.	7	12	Rs. 9.4.0	111	12 ck	Rs. 9.4.0	111	—	—	
Cutting one pulley recessed	8	2.5	6.8.0	16	2.5	6.8.0	16	—	—	
Supplying and fixing iron pulleys.	9	3	LS.	15	3	LS.	15	—	—	
Supplying and fixing iron foot rest	10	LS	LS.	20	35	LS	50.	30	—	
Removing stones of waste.	11	LS	—	70	LS	—	—	—	70	
Pulley Supplies and Contingencies	12	LS	—	135	LS	—	265	130	—	
				4400			6700	2748	448	
							4400			
Excess amount =							2300/-			

28.6.54
SO Pulley.

L. A. Carlton 27.6.54
Asst. Engineer Cl.
Mayabunder

Construction of Buildings for the Primary Health Centre at Bajpe - Revised estimate for well —.

ESTIMATE FORM.—Comparative Statement of Differences. P.W.D. V-18(inner)—46,406—20-6-52.

Description of work.	Item No.	Original estimate.			Revised estimate.			More.	Less.	Explanation of difference.
		Quantity.	Rate.	Amount.	Quantity.	Rate.	Amount.			
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)
earth work - open well excavation Complying with client's clauses of 88 well sinking	I		Rs.	Rs.		Rs.	Rs.			
1st depth in ordinary gravel		1200	21.6.0	24	1207	21.6.0	26	2	Nil	
2nd depth in soft disintegrated rock		950	43.3.0	42	924	43.3.0	40	—	2	
3rd do - do - do		950	65.0.0	62	924	65.0.0	60	—	2	
4th do - do - do		950	97.7.0	87	924	97.7.0	90	3	0	
5th do - do - do		950	146.3.0	139	924	146.3.0	135	—	4	
6th do in hard gravelly soil		500	162.5.0	81	924	162.5.0	150	69	—	
7th do - do - do		—	—	—	924	243.7.0	226	226	—	
8th do - do - do		—	—	—	924	365.2.0	338	338	—	
9th do do do		—	—	—	308	547.4.0	169	169	—	
9th do in clay and gravel		—	—	—	462	486.10.0	224	224	—	
Sinking well in loose sand or sand 33-36	II	3	38.10.0	116	—	—	—	—	116	
do - do - 36-42		6	40.10.0	244	—	—	—	—	244	
do - do - 53-58		—	—	—	5	57.0.0	285	285		
RC work for well kerb 1:2:4	3	44	4.4.0	187	42.20	4.4.0	178	—	10	
Laterite masonry in CM 1:5 for steining	4	1750	127.4.0	2227	2750	127.4.0	3499	1272	—	
do - do - for filter drain etc.		350	121.0.0	422	350	121.0.0	423	—	—	
Concrete broken stone in Cement mix 1:5	5	250	91.0.0	228	250	91.0.0	228	—	—	
Plastering with Cement mortar 1:4	6	1500	11.8.0	173	1500	11.8.0	173	—	—	
				4033			6298	2586	378	

C.F. 32 ( )—70,10,558—20-1-54.

Department | Received ..... Registered .....

From (Name) Sri.H.Narasimha,

Designation Project Executive Officer,

Station South Kanara, Mangalore.

To

The Director of Community Projects & Ex.Officio Addl. Secretary to Government of Madras.

ADDITIONAL ASST. SECRETARY TO GOVERNMENT
2 AUG 1954
PUBLIC DEPARTMENT

Enclosures Ref.C. No. 1625/54-C. dated 27-7-1954. 195 .

Sir,

Community Projects--South Kanara--Block No.I--Primary Health Centre at Bajpe--Construction of a well--Full Payment for the extra work over and above the sanctinned estimate--Regarding--Further Report--Submitted.

Ref: My report Ref.C.No.206/52-B dated 18-7-1954.

In continuation of my report cited, I submit that a meeting of the Bajpe Hospital Building Construction Committee was held on 25-7-54 at which almost all members matters touching the hospital work ~~xx~~ especially the well work was discussed by the members. As already indicated in my report cited, the committee has unanimously resolved to request the Government for sanctioning full payment for ~~the~~ the extra work done for the deepening of the well on the ground that it is not possible for the Committee to raise any contribution from the~~ppx~~ public during these lean months. An extract of the resolution of the Committee requesting full payment for the well work (extra) is enclosed for kind perusal.

I therefore request that orders on my reference requesting the sanction of extra ~~xp~~ expenditure, may kindly be passed and communicated to me at an early date.

Yours faithfully,

Project Executive Officer 29.7.54

2917

Extract from ~~Copy of~~ the proceedings of the Executive Committee of the Bajpe Dharma Aspathre Sangh held on 25-7-54 at the Community Hall Buimlding, Bajpe.

--

1. Resolved that the amount of expenditure relating to the extra work involved in the construction of the well over and above the original ~~e~~stimated amount be met in full by the Community Project, in view of the fact that raising additional funds from the public at this time of the year is practically not possible and that the committee has no funds to spare for the additional work.

2. Resolved that the Project Executive Officer be requested to settle the payment in regard to the roofing at full rate, as ~~early~~ only part payment has been made now, as expeditiously as possible.

3. Resolved further that the work relating to the construction of the septic ~~xxxkx~~ tank latrine, gate with pillars, forming the approaches, and levelling be taken up at 50% contribution basis as soon as revised sanction order for the well as prayed for in resolution No:1 is received and the bill due in respect of resolution No. 2 is passed.

P.T.O.

4. Resolved that it is necessary to have a formal opening of thenew building and the date of the opening ~~xxx~~ function be fixed as soon as the remaining items of work are completed.

/-True Copy-/

Project-Executive Officer

Pub (RDP I) 1/

Memo No 81301 Pub (RDP I) 54-2 dt. 7 9/54

Bl. issued 8/9/54 7/9/54

Sub:- Cls- S. Kanara Area- Health and Sanitation - Construction of a Primary Health Centre at Bappe - Construction of well - Payment for extra work done.

Ref- from the PEO. Mangalore ref. C. No 1625/54-C dated 27-7-54.

The PEO. Mangalore is informed that the following information is needed before the recommendations made in his letter cited can be examined

~~1) The Comparative Statement furnished by the PEO/ Mangalore Covers only the cost of the well. As the~~ Sanction has already accorded in GO Ms 1405- Pub (CP) dated 27-5-53 ~~was~~ for half the cost of the well work it is necessary to examine the extent of ultimate Commitment in regard to the work both by Govt. and the beneficiaries. The PEO is therefore requested to furnish a revised estimate including all the items covering Sub works ~~and items of work~~ already done and remaining to be done.

(the remaining half being contribution from the beneficiaries)

2) The original sanction has been accorded on the understanding that the cost of the work will be borne equally between C.P. funds and the beneficiaries. It should therefore be reported to what extent and amount the beneficiaries are prepared to share in the ultimate cost of the work. The hospital Committee may therefore be asked to state clearly the total amount of expenditure

to bear
they can afford, ~~so that similar requests are not made and~~ so that the ~~remaining~~ balance amount required may be met from C.P. funds, ~~works may be carried out expeditiously~~.

The PEO Mangalore is requested to submit his report in ~~ten days~~ the matter by not later than 25.9.54. ~~to~~
~~.9.54~~
~~Draft~~.

80/69/54

19/9/54

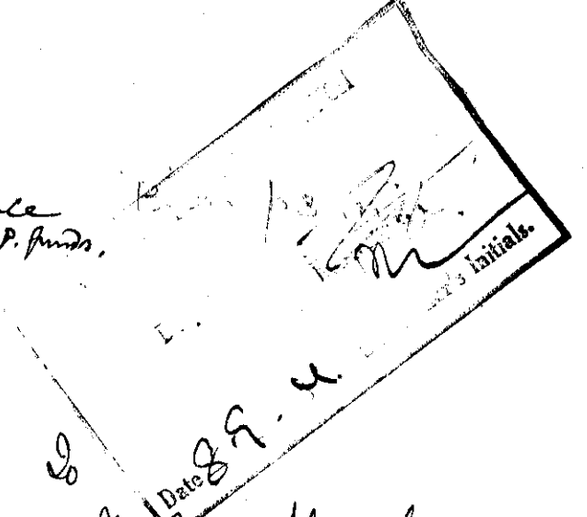

To

The P.E.O. Mangalore
S.K. Dist

25-9-54
R.D. ~~15 days.~~

Ecv. issued on 22x53
Repayable by 15-11-54 } 80/22x53

By Express Delivery.
Ref.C.No.1625/54-C.

Project Executive Office, S.K.,
Mangalore, dated 22-10-1954.

From
Sri. H. Narasimha,
Project Executive Officer,
South Kanara, MANGALORE.

To
The Director of Community Development,
MADRAS.

Sir,

COMMUNITY PROJECTS--South Kanara--Health & Rural Sanitation--Construction of a Primary Health Centre at Bajpe--including a well--Payment of Extra Cost--Further report--Submitted.

Ref: Govt.Memorandum No.81301 Pub. (R.D.P.)V/54-2, dated 7-9-54.

A copy of the Asst. Engineer's report together with its enclosure is enclosed.

2 The total cost of the work as per sanctioned estimate is Rs.27300/- out of which Rs.13650/- was sanctioned from Community Project funds. The total value of work actually done will be limited to Rs.27300/- as detailed in the statement submitted by the Asst. Engineer. Savings effected under the items excluding the well will be equivalent to the extra expenditure incurred for the well work. But by paying the full value of the extra work involved in the well work, the Community Project Share will be Rs.14750/- as against the sanctioned amount of Rs.13650/-. Thus, the additional amount to be sanctioned comes to Rs.1100/-.

3 But, as the Asst. Engineer reports, the people's contribution will be only Rs.12550/- as against the expected amount of Rs.13650/-. If this contribution is forthcoming from the people, there will be no need to sanction any extra amount from Community Project funds. But, from the attitude of the beneficiary it is difficult to expect the full contribution of Rs.13650/-. I, therefore, recommend that the Government may be pleased to sanction an additional expenditure of Rs.1100/- in this case.

Yours faithfully,

Project Executive Officer.

Copy of letter Ref.1239/E/54, dated 16-10-1954 from the Asst. Engineer(C.T.) Mangalore addressed to the Project Executive Officer.

COMMUNITY PROJECTS--South Kanara--Block I--Primary Health Centre at Bajpe--Construction of building--Revised estimate--Submitted.
Ref: Project Executive Officer's Ref.C.No.1625/54-C, dated 17-9-54.

I am herewith submitting the comparative statement for the work mentioned above as called for in the No. cited above.

The total amount of the revised estimate remains unaltered due to savings in items 1, 5 and 6, even though the remaining items, viz. 2, 3 and 4 have exceeded the sanctioned amount. But due to the unwillingness of the beneficiaries to contribute on 50% basis on the extra expenditure involved in the construction of well on the plea that the maximum amount the committee could afford to spend is only Rs.2200/- as originally contemplated. Further sanction has to be obtained to an extent of Rs.2300/- (vide statment enclosed).

P.T.O.

The Supervisor reports that the original sanction order (G.O.Ms.No.1405 dated 27-5-1953) has already been handed over to Sri.Narayana Nair, clerk in your office.

It is also brought to notice that the people's contribution, as per present proposal will be only Rs.12,550/- as against the grand total of Rs.13650/- as originally proposed. So there seems no justification for the committee to claim this extra full payment for the extra work of well, now called for. The proportionate extra cost will be only Rs.1100/- as against this present saving of Rs.1100/- (13650 - 12550/-).

/-True Copy/-

JC/22-10-54.

Project Executive Officer.
23.10.54.

224

Primary Health centre Bajpe. Statement of expenditure and a amount requiring same

Community Projects
South Kanara area
Block I.

Discription of work	Estimated amount Rs	Peoples contribution Rs.	Expenditure from C.P. Funds Rs	Total Value of work done Rs.	Peoples contribution Rs.	Amount of expenditure from C.P. Funds Rs.	Extra amount involved Rs.	Remarks.
1) Outpatient Dispensary	9000/-	4500/-	4500/-	8200/-	41	4100		Actuals as per execution 50% contribution
2) A ward of Six beds	8900/-	4450/-	4450/-	9000/-	45	4500		— do —
3) Kitchen block	2000/-	1000/-	1000/-	2200	110	1100		— do —
4) Well of 40ft. diameter.	4400	2200/-	2200/-	6600	22	4400	2200	Due to extra depth of 18ft. Full contribution
5) Sanitary fittings including Septic tank etc.	1500	750/-	750/-	500 (Proposed)	25	250		As per working estimate.
6) Forming road inside Hospital compound, providing a gate and pillers etc.	1500	750/-	750/-	800 (Proposed)	40	400		Rough cost for gate & pillers and the road.
	27300	13650	13650	27300	125	14750	2200	

Assistant Engineer,
Community Projects
Mangalore.
16-10-54

Report to accompany the revised estimate for "Construction of Hospital Buildings at Bajjhe".

The estimate is revised as the actual execution with certain deviation found essential during execution adopting the revised rate. The construction of the Buildings viz① Out patient Dispensary ② Ward of six beds and ③ kitchen & Well is almost completed and the full payment has been made for the same. Items which are left to be executed are finishing the terrace and floor of out patient dispensary and providing wooden shelves the kitchen & Store for which necessary provision is made in the estimate.

1) The original sanction for the Out patient dispensary is for Rs 9000/- But the actual cost as the payment made including the same to the time provided comes to Rs 8200/- and thus there is a savings of Rs 800/-

2) Ward of six Beds:- The original sanction is for Rs 8900/- The present cost as per R/E is Rs 9000/- which is due to the provision of the extra item now provided for which no provision was made in the original estimate. Hence there is an excess of Rs 100/- The Building is completed.

3) kitchen:- The original sanction is Rs. 2000/- But the actual cost as executed comes to Rs 2200/- and hence there is an excess of Rs 200/- The Building is almost completed excepting joining wall & shutters of which is intended in the Revised estimate

4) Well of 10'0 Dia:- The original sanction is for Rs 4400/- for a depth of 40'-0. But during execution it was found necessary to increase the depth to 58'-0 as there was no trace of water up to 50'0. Sinking work was stopped at 58'0 due to boring strata below. Due to this extra depth of 18'0 there is an excess expenditure of Rs 2200/-. The revised estimate is for Rs 6600/- Details Steining for a depth of 36'0 has been completed and thus the expenditure so far is Rs 3980/- and balance of work to be done is steining from depth of 22'0 with necessary platform parapet wall etc. which is also included in the R/E

5) Septic tank Latrine:- In the original estimate a Lump sum of Rs 1500/- was provided for Sanitary fittings and Septic tank etc. Now it is proposed to construct a Deep leach type latrine with a Concrete ring well covered with Sanitary fittings approved design & drawing which comes to 500/- as per detailed working estimate. Hence there is a savings of Rs 1000/- under this head

6) Fencing road including gate etc:- The original sanction under this sub head is for Rs 1500/- The main work of the

D.P.H II-14. 20,006—20-12-52.

ORIGINAL.

K ಫಾರ್ಮ್ (36 ನೇ ಅನುಚ್ಛೇದ).

ನೋಟೀಸು-

1920 ನೇ ಇಸವಿಯ ಮದ್ರಾಸ್ ಲೋಕಲ್ ಬೋರ್ಡುಗಳ ಆಕ್ಟಿನ 137 ನೇ ಮತ್ತು 200 ನೇ ಪ್ರಕರಣಗಳ ಮೇರೆಗಿನ ಕ್ರಮಗಳು.

ನ

ಹೆತ್ತವ / ಸಂರಕ್ಷಕ ನಾದ ಗೆ

ಮಗುವಿನ ಹೆಸರು

ವಯಸ್ಸು

ವಾಸಸ್ಥಳ

ಗ್ರಾಮ ಮುಖ್ಯಸ್ಥನಿಂದ / ಯೂನಿಯನ್ ಪ್ರೆಸಿಡೆಂಟನಿಂದ ಕೊಡಲ್ಪಟ್ಟ ನೋಟಿಸಿಗನುಸಾರ

ವಾಗಿ ಮೇಲಿನ ಮಗುವನ್ನು ದಾಕು ಹಾಕಲ್ಪಡುವ / ಸಂದರ್ಶಿಸಲ್ಪಡುವ ಬಗ್ಗೆ ಹಾಜರುಮಾಡಲು

ನೀನು ತಪ್ಪಿರುವುದರ ದೆಸೆಯಿಂದ, 19 ನೇ ಇಸವಿ

ಲ್ಲಿ ಪೂರ್ವಾಹ್ನ / ಅಪರಾಹ್ನ ಲ್ಲಿ ಲ್ಲಿ ದಾಕು ಹಾಕಲ್ಪ / ಸಂದರ್ಶಿಸಲ್ಪ

ಡುವ / ಡುವ ಬಗ್ಗೆ ಸದರೀ ಮಗುವನ್ನು ಹಾಜರುಮಾಡಬೇಕಾಗಿ ನಿನಗೆ ಈ ಮೂಲಕ ವಿಧಿಸೋಣಾಗುತ್ತಿದೆ; ನೀನು ಮೇಲಿನ ಕಾಲದಲ್ಲಿ ಮತ್ತು ವೇಳೆಯಲ್ಲಿ ಸದರೀ ಮಗುವನ್ನು ಹಾಜರುಮಾಡದಿದ್ದು, ಆ ಕುರಿತು ಸಮರ್ಪಕವಾದ ಸಬೂಬು ತೋರಿಸಲು ತಪ್ಪಿದ ಪಕ್ಷದಲ್ಲಿ, ಮೇಲಿನ ಕ್ರಮಗಳ ಮೇರೆಗೆ ನೀನು ಶಿಕ್ಷಾರ್ಹ ವ್ಯವಹರಣೆ ನಡೆಸಲ್ಪಡುವುದಕ್ಕೆ ಗುರಿಯಾಗುವೆಯೆಂದು ತಿಳಿಯುವ್ವದು.

ವ್ಯಾಕ್ಸಿನೇಶೇಟರ್.
ಡಿಸ್ಟ್ರಿಕ್ಟ್ ಹೆಲ್ತ್ ಇನ್‌ಸ್ಪೆಕ್ಟರ್.

ರೇಂಜ್.

ತಾರೀಖು 19 .

D.P.H. II-14.

DUPLICATE.

K ಫಾರ್ಮ್ (36 ನೇ ಅನುಚ್ಛೇದ).

ನೋಟೀಸು-

1920 ನೇ ಇಸವಿಯ ಮದ್ರಾಸ್ ಲೋಕಲ್ ಬೋರ್ಡುಗಳ ಆಕ್ಟಿನ 137 ನೇ ಮತ್ತು 200 ನೇ ಪ್ರಕರಣಗಳ ಮೇರೆಗಿನ ಕ್ರಮಗಳು.

ನ

ಹೆತ್ತವ / ಸಂರಕ್ಷಕ ನಾದ ಗೆ

ಮಗುವಿನ ಹೆಸರು

ವಯಸ್ಸು

ವಾಸಸ್ಥಳ

ಗ್ರಾಮ ಮುಖ್ಯಸ್ಥನಿಂದ / ಯೂನಿಯನ್ ಪ್ರೆಸಿಡೆಂಟನಿಂದ ಕೊಡಲ್ಪಟ್ಟ ನೋಟಿಸಿಗನುಸಾರ

ವಾಗಿ ಮೇಲಿನ ಮಗುವನ್ನು ದಾಕು ಹಾಕಲ್ಪಡುವ / ಸಂದರ್ಶಿಸಲ್ಪಡುವ ಬಗ್ಗೆ ಹಾಜರುಮಾಡಲು

ನೀನು ತಪ್ಪಿರುವುದರ ದೆಸೆಯಿಂದ, 19 ನೇ ಇಸವಿ

ಲ್ಲಿ ಪೂರ್ವಾಹ್ನ / ಅಪರಾಹ್ನ ಲ್ಲಿ ಲ್ಲಿ ದಾಕು ಹಾಕಲ್ಪ / ಸಂದರ್ಶಿಸಲ್ಪ

ಡುವ / ಡುವ ಬಗ್ಗೆ ಸದರೀ ಮಗುವನ್ನು ಹಾಜರುಮಾಡಬೇಕಾಗಿ ನಿನಗೆ ಈ ಮೂಲಕ ವಿಧಿಸೋಣಾಗುತ್ತಿದೆ; ನೀನು ಮೇಲಿನ ಕಾಲದಲ್ಲಿ ಮತ್ತು ವೇಳೆಯಲ್ಲಿ ಸದರೀ ಮಗುವನ್ನು ಹಾಜರುಮಾಡದಿದ್ದು, ಆ ಕುರಿತು ಸಮರ್ಪಕವಾದ ಸಬೂಬು ತೋರಿಸಲು ತಪ್ಪಿದ ಪಕ್ಷದಲ್ಲಿ, ಮೇಲಿನ ಕ್ರಮಗಳ ಮೇರೆಗೆ ನೀನು ಶಿಕ್ಷಾರ್ಹ ವ್ಯವಹರಣೆ ನಡೆಸಲ್ಪಡುವುದಕ್ಕೆ ಗುರಿಯಾಗುವೆಯೆಂದು ತಿಳಿಯುವ್ವದು.

ವ್ಯಾಕ್ಸಿನೇಟರ್.
ಡಿಸ್ಟ್ರಿಕ್ಟ್ ಹೆಲ್ತ್ ಇನ್‌ಸ್ಪೆಕ್ಟರ್.

ರೇಂಜ್.

ತಾರೀಖು 19 .

D.P.H. II-14.

TRIPLICATE.

K ಫಾರ್ಮ್ (36 ನೇ ಅನುಚ್ಛೇದ).

ನೋಟೀಸು.

1920 ನೇ ಇಸವಿಯ ಮದ್ರಾಸ್ ಲೋಕಲ್ ಬೋರ್ಡುಗಳ ಆಕ್ಟಿನ 137 ನೇ ಮತ್ತು 200 ನೇ ಪ್ರಕರಣಗಳ ಮೇರೆಗಿನ ಕ್ರಮಗಳು.

ನ

ಹೆತ್ತವ / ಸಂರಕ್ಷಕ ನಾದ ಗೆ

ಮಗುವಿನ ಹೆಸರು

ವಯಸ್ಸು

ವಾಸಸ್ಥಳ

ಗ್ರಾಮ ಮುಖ್ಯಸ್ಥನಿಂದ / ಯೂನಿಯನ್ ಪ್ರೆಸಿಡೆಂಟನಿಂದ ಕೊಡಲ್ಪಟ್ಟ ನೋಟಿಸಿಗನುಸಾರ

ವಾಗಿ ಮೇಲಿನ ಮಗುವನ್ನು ದಾಕು ಹಾಕಲ್ಪಡುವ / ಸಂದರ್ಶಿಸಲ್ಪಡುವ ಬಗ್ಗೆ ಹಾಜರುಮಾಡಲು

ನೀನು ತಪ್ಪಿರುವುದರ ದೆಸೆಯಿಂದ, 19 ನೇ ಇಸವಿ

ಲ್ಲಿ ಪೂರ್ವಾಹ್ನ / ಅಪರಾಹ್ನ ಲ್ಲಿ ಲ್ಲಿ ದಾಕು ಹಾಕಲ್ಪ / ಸಂದರ್ಶಿಸಲ್ಪ

ಡುವ / ಡುವ ಬಗ್ಗೆ ಸದರೀ ಮಗುವನ್ನು ಹಾಜರುಮಾಡಬೇಕಾಗಿ ನಿನಗೆ ಈ ಮೂಲಕ ವಿಧಿಸೋಣಾಗುತ್ತಿದೆ; ನೀನು ಮೇಲಿನ ಕಾಲದಲ್ಲಿ ಮತ್ತು ವೇಳೆಯಲ್ಲಿ ಸದರೀ ಮಗುವನ್ನು ಹಾಜರುಮಾಡದಿದ್ದು, ಆ ಕುರಿತು ಸಮರ್ಪಕವಾದ ಸಬೂಬು ತೋರಿಸಲು ತಪ್ಪಿದ ಪಕ್ಷದಲ್ಲಿ, ಮೇಲಿನ ಕ್ರಮಗಳ ಮೇರೆಗೆ ನೀನು ಶಿಕ್ಷಾರ್ಹ ವ್ಯವಹರಣೆ ನಡೆಸಲ್ಪಡುವುದಕ್ಕೆ ಗುರಿಯಾಗುವೆಯೆಂದು ತಿಳಿಯುವುದು.

ವ್ಯಾಕ್ಸಿನೇಟರ್.
ಡಿಸ್ಟ್ರಿಕ್ಟ್ ಹೆಲ್ತ್ ಇನ್‌ಸ್ಪೆಕ್ಟರ್.

ರೇಂಜ್.

ತಾರೀಖು 19 .

executed under this item to provide a gate with pillars and form a road from the gate to the Hospital.

The soil being very hard ~~and rocky~~ only cutting of Contour out-crop and filling with earth is required for forming a small length of road. The total cost of forming this road including providing a gate with pillars will come to Rs 800/- only. As such there will be a savings of Rs 700/- under this item.

The total amount of the Revised estimate (vide above statement) comes to Rs 27300/- and there is no extra expenditure against the original sanction of Rs 27300/-.

B. Sadasivam
2.x.54
J.O. Madras.

Primary Health Centre at Bajpe

(A) Out Patient Block.

ESTIMATE FORM.—Comparative Statement of Differences.

P.W.D. V-18(inner)—46,406—20-6-52.

Description of work.	Item No.	Original estimate. Quantity.	Rate.	Amount.	Revised estimate. Quantity.	Rate.	Amount.	More.	Less.	Explanation of difference.
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)
Earth work excavation for foundation in ordinary ground	1	600	37 RS 12-0	RS 23	520	37 RS 12-0	20 RS ~~19~~	—	3 ~~2~~	
Earth work excavation in hard gravelly soil.	a	900	42-12-0	38	780	42-12-0	33	—	5	
Cement Concrete 1:5:10.	2	600	91-0-0	541	520	90-8-0	471	—	70	
Laterite masonry in Cement mortar 1:5 . .	3	2200	121/=	2662	2134	121/=	2582	—	80	
Damp proof course in C.M. mortar 1:3 - 3/4" thick	(b)	400	21-0-0	84	395	20/-	79	—	5	
Refilling with excavated earth	c	750	10-0-0	8	688	10/-	7	—	1	
Plastering with Cement mortar 1:5 - 1/2 thick	4	3350	11-5-0	379	3924	10-0-0	392	13	—	
Flooring with C. Concrete 4" thick 1:5:10 and topping	5	390	42/=	164	350	42/=	147	—	17	
Flooring with C. Concrete 1:5:10 plastered with 1cm Cement	(6)	370	52/=	192	338	52/=	176	—	16	
Roofing with Mangalore tiles over Ceiling tiles.	6	1460	75/=	1097	1352	66-2-0	894	—	63.	
Country wood wrought and fixed.	7	100	4-0-0	1100	78-30	11-0-0	862	—	238	
Country wood fully panelled door with glazing.	8a	2	103-12-0	208	2	103-12-0	208	—	—	
Country wood half door panelled.	b	2	40-40	81	2	40-40	81	—	—	
Cw Windows with glazed head iron bars 2-6×5 1/2	c	2	72-80	145	2	72-80	145	—	—	
Cw. windows glazed with iron bars 2-6×4-1 1/2	d	2	45-00	90	2	45/-	90	—	—	
Do Do Do Do 4-0×4 1/2	e	1	67-00	67	1	67/=	67	—	—	
				6839			6247+9	13	607	+9
										910

ESTIMATE FORM.—Comparative Statement of Differences. P.W.D. V-18 (inner)—46,406—20-6-52

Description of work.	Item No.	Original estimate.			Revised estimate.			More.	Less.	Explanation of difference.
		Quantity.	Rate.	Amount.	Quantity.	Rate.	Amount.			
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)
			Rs.	Rs. 6839		Rs.	Rs. 6254 ~~6245~~	13	598 ~~607~~	
Country wood fixed window	f	2	42/=	84	2	42/=	84	—	—	
C.W. Semicircular ventilators glazed.	g	2	20/8	41	2	20/8	40		1	
C.W. trellis door painted with grey paint	h	2	69-4-0	139	3	69-4-0	208	69	—	
Country wood battens work including painting	i	250	1-10-6	414	254	1-10-6	421	7	—	
C.W. Cupboard with glazed shutters	j	4	80/-	320	4	80/=	320	—	—	
Country wood screw	k	1	LS -	25	-	LS	25	—	—	
C.W. shelf in the Dispensary	9(a)		LS	40		LS	40	—	—	
R.C. flat sun shade.	10	32	3-5-0	106	32	3-5-0	106	—	—	
R.C. lintels over doors and windows	10(a)	29	7-8-0	218	23-88	7-8-0	179	—	39	
Painting with light grey paint.	11	450	8/=	36	551	8/=	44	8	—	
For fluctuations in rate.	12		LS.	120	—	—	-	-	120.	
For reinforcement items of work.	13	—	LS.	220	—	LS.	50	—	170	
Painting with polyurethane	13(a)	—	—	—	1004	4-12-0	48	48	—	
Petty supervision and contingencies	14	—	LS.	398	—	LS	~~390~~ 381	—	~~8~~ 17	
			Total.	9000			8200	145	945	

Ward of Six Beds.

ESTIMATE FORM.--Comparative Statement of Differences.

P.W.D. V-18(inner)—46,406—20-6-52.

Description of work. (1)	Item No. (2)	Original estimate. Quantity. (3)	Rate. (4)	Amount. (5)	Revised estimate. Quantity. (6)	Rate. (7)	Amount. (8)	More. (9)	Less. (10)	Explanation of difference. (11)
Earth work excavation in ordinary gravel.	1	1500	3/12	RS 57	1357	3/12-0	RS 51	—	6	
Do - Do in hard gravelly soil.	(6)	500	42-12-0	21	256	42-12-0	11	—	10.	
Concrete broken stone in Cement mortar 1:5:10.	2	720.	91-0-0	655	707	90-8-0	640	—	15	
Hard Laterite masonry in Cement mortar 1:5.	3	2525	121/=	3055	2722	121/=	3294	239	—	
Damp proof course in Cement mortar 1:3	(6)	350	21/=	74	305	20/=	61	—	13	
Filling with excavated earth	c.	1400.	10-0-0	14	1023	10/=	10	—	4	
Plastering with Cement mortar 1:5 - ½" thick	4	3100.	1-5-0	351	4314	10-0-0	431	80	—	
Flooring with Concrete 4" thick and top plastered.	5	980	42/=	412	~~900~~ 862	42/=	~~378~~ 362	—	~~34~~ 50	
Roofing with Clearglaze tiles over Ceiling tiles	6.	1884	75/=	1413	1385	66-2-0	916	—	497	
Roofing with plain Clearglaze tiles over C.W. purlins	6(a)	—	—	—	605	44-4-0	268	268	—	
Country wood wrought and put up	7	134-60	11-0-0	1481	114-0	11/=	1254	—	227.	
King post truss of 20' clear span	7(b)	1	172-90	173	1	172-90	173	—	—	
C.W. doors framed and planked 3-6×7-0.	8	1	63-80	64	1	63-80	64	—	—	
C.W. ventilators. 2-6×1-6.	(6)	2	20-80	41	2	20-80	41	—	—	
C.W. windows glazed with iron bars 2-6×4-1½	c	3	45-00	135	4	45/=	180	45	—	
C.W. windows glazed with iron bars 4-0×5-0.	d	4	81-4-0	325	3	81-4-0	244	—	81	
				8271			~~8076~~ 8000	632	~~887~~ 903	Co.

ESTIMATE FORM.—Comparative Statement of Differences. P.W.D. V-18 (inner)—46,406—20-6-52

Description of work.	Item No.	Original estimate.			Revised estimate.			More.	Less.	Explanation of difference.
		Quantity.	Rate.	Amount.	Quantity.	Rate.	Amount.			
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)
		B. forward.	RS.	RS. 8271		RS.	8000 RS.	632	903	
C.W. Panelled doors with arches etc. 4-0 x 7-0	(e)	—	--	—	2	81-8-0	163	163	—	
Do Do - Do - 3-0 x 6-9	(f)	—	—	—	1	59-0-0	59	59	--	
C.W. Leaf board and panelled door 2-0 x 6-6	(g)	—	—	—	2	36-11-0	74	74	-	
Cement broken stone in Cm.star 1:2:4.	h	—	—	—	1.63	180/-	3	3	—	
R.C. lintels over doors and windows	i	—	—	—	23.56.	7-8-0	177	177	—	
Painting with grey paint.	9	340	8/-	27	594	8/-	48	21	—	
Unforseen items of work Soakas drains etc.	10	L.S	—	212	—	L.S.	50	—	162	
Painting with Soligneum.	10a	—	—	—	1670	4/12	80	80	—	
Petty Supervision and Contingencies.	11.	L.S	—	390	L.S	—	346 ~~330~~	—	~~44~~	
		Total		8900			9000	1209	1109	
					Rs. 0					

KITCHEN BLOCK

ESTIMATE FORM.—Comparative Statement of Differences.

P.W.D. V-18(inner)—46,406—20-6-52.

Description of work. (1)	Item No. (2)	Original estimate. Quantity. (3)	Rate. (4)	Amount. (5)	Revised estimate. Quantity. (6)	Rate. (7)	Amount. (8)	More. (9)	Less. (10)	Explanation of difference. (11)
			Rs.	Rs.		Rs.	Rs.			
Earth work excavation in ordinary gravel.	1	500	27.12-0	69	409	37.12-0	46	—	3	
Concrete broken stone in Cement mortar 1:5:10.	2	150	91-0-0	137	164	90.8-0	148	11	—	
Hard laterite masonry in Cement mortar 1:5.	3	550	121/=	665	789	121/=	955	290	—	
Damp proof course in Cement mortar 1:3.	6	75	21/=	16	95	20/=	19	3	—	
Filling with excavated earth.	c.	175	10/=	2	200	10/=	2	—	—	
Plastering with Cement mortar 1:5.	4	1000	11.5.0	113	1157	10/=	116	3	—	
Flooring with 4" thick Concrete.	5	190	42/=	80	135	42/=	57	—	23.	
R.C. Lintels over doors and windows.	5(a)	10.90	7.8-0	79	11.06	7.8-0	83	4	—	
Roofing with Mangalore tiles on Ceiling tiles	6	340	75/=	233	349	66.2-0	231	—	2	
Roofing with plain Mangalore tiles on C.I. rafters	6(A)	—	—	—	55	44-4-0	24	24	—	
Country wood wrought and fixed up	7	17.5.	11.0.0	193	20.14	11/=	222	29	—	
Country wood doors framed and planked	8	1	63.8-0	64	1	65.8-0	66	2	—	
Country wood windows framed and planked.	8(b)	2	40/=	80	2	40/=	80	—	—	
Country wood wrought and fixed up for furniture work	9	5.5	11/-	61	5.5	11/=	61	—	—	
Painting with grey paints	10	150	8/.	12	132	8/.	11	—	1	
				1754			2091	366	29	60.

ESTIMATE FORM.—Comparative Statement of Differences. P.W.D. V-18 (inner)—46,406—20-6-52

Description of work. (1)	Item No. (2)	Original estimate. Quantity. (3)	Rate. (4)	Amount. (5)	Revised estimate. Quantity. (6)	Rate. (7)	Amount. (8)	More. (9)	Less. (10)	Explanation of difference. (11)
			Rs.	1754 Rs.		Rs.	2091 Rs.	366	29	
Painting with Soligineum two Coats	10(a)	—	—	—	255	4:12 0	12	12	—	
Fluctuations in rate.	11	Ls	—	100	—	—	—	—	100.	
For excavation item of work.	12	Ls.		60	—	Ls.	20	—	40.	
Pulley, suspension and Centring gear	13	Ls.		86	Ls	—	77	—	9	
		Total.		2000			2200.	378	178.	
Well of 10'-0 Diameter.										
Earth Cords for open well excavation Company rate reduced										
Clauses of the well Sinking —										
1st depth in ordinary gravel.	1	1200	21.6-0	24	1207	21.6.0	26	2	—	
2nd depth in soft disintegrated rock.	a	950	43.5.0	42	924	43.5.0	40	—	2	
3rd do. do. do.	b	950	65.0.0	62	924	65.0.0	60	—	2	
4th do. do. do.	c	950	97.7.0	87	924	97.7.0	90	3	—	
5th do do do	d	950	146.3.0	139	924	146.3.0	135	—	4	
6th depth in hard gravelly rock	e	500	162.5.0	81	924	162.50	150	69	—	
7th do do do	f	—	—	—	924	263.70	226	226	—	
8th do do do.	g	—	—	—	924	365.20	338	338	—	
				435			1065	638	8	60.

ESTIMATE FORM.—Comparative Statement of Differences. P.W.D. V-18(inner)—46,406—20-6-52.

Description of work.	Item No.	Original estimate.			Revised estimate.			More.	Less.	Explanation of difference.
		Quantity.	Rate.	Amount.	Quantity.	Rate.	Amount.			
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)	(10)	(11)
				435			1085	638	8	
9" depth in hard gravelly soil	—	—	RS. —	RS. —	308	RS. 547.1.0	RS. 169	169	—	
9" depth in clay and gravel		—	—	—	462	483.10.0	224	224	—	
Sinking well in loose soil (zone) 33-36.	2	3	38.10.0	116	—	—	—	—	116	
Do — Do — 36-42	3	6	40.10.0	244	—	—	—	—	244	
Do — Do — 53-58	3(a)	—	—	—	5	57/=	285	285	—	
R.C. work for well kerb	4	44	4-4-0	187	42.2	4.4.0	178	—	9-1	
Lateritic masonry in Cement mortar 1:5.	5	1750	127.4.0	2227	2750	127.4.0	3499	1272	—	
Do — Do for pillars drain retaining.	6	350	121.0.0	423	350	121/=	423	—	—	
Cement broken stone in Cement mortar 1:5	7	250	91/=	228	250	91/=	228	—	—	
Plastering with Cement mortar 1:4	8	1500	1.8.0	~~177~~ 173	1500	1.8.0	173	—	—	
Rounding wood (wrought and put up.	9	12	9.4.0	111	12	9.4.0	111	—	—	
Curb stone fully dressed.	10	2.5	6.8.0	16	2.5	6.8.0	16	—	—	
Supplying and fixing iron pulley . .	11	3	L.S.	15	3	L.S.	15	—	—	
Supplying and fixing iron foot rest . .	12	19	L.S.	20	30	L.S.	50	30	—	
Unforseen items of work.	13	L.S.	—	70	—	—	—	—	70	
Petty supervision and Contingencies	14		L.S.	139	—	L.S.	164	29	—	
			Total	4400			6800	2647	447.	

P.C.O.

GENERAL ABSTRACT

ESTIMATE FORM—Comparative Statement of Differences.

P.W.D. V-47.

Description of work. (1)	Item No. (2)	Original Estimate. Quantity. (3)	Rate. (4)	Amount. (5)	Revised Estimate. Quantity. (6)	Rate. (7)	Amount. (8)	More. (9)	Less. (10)	Explanation of difference. (11)
			Rs.	Rs.		Rs.	Rs.	Rs.	Rs.	
Outpatient Dispensary	1	—	—	9000	—	—	8200	—	800	Actuals - as per execution
Ward of Six Beds.	2	—	—	8900	—	—	9000	100	—	As per actual execution.
kitchen Store.	3	—	—	2000	—	—	2200	200	—	Do — Do —
Well of 10'0 dia.	4			4400	—	—	6600	2200	—	Due to extra Depth of 18'0
Sanitary fitting including septic tank etc	5		Ls -	1700	—	Ls.	700	—	1000	as per actuals.
fencing road metal boundary gate and pillars etc	6	—	Ls.	1900	—	Ls.	900	—	700	Rough cost for gate and pillars and fencing.
Total ..				27300			27300	2500	2500	
Deduct amount of estimate already sanctioned		—	—	—	—	—				
Net amount requiring sanction — —		—	—	—	—	—	NIL			

Sanctioned for Rs. (_____)_____

_____ only

in supersession of C.R. No._____ of_____

3.X.54

Executive Engineer.

Superintending Engineer.

G.O.Ms.No 2316/54 dt 26/11/54
~~Home No. 81301 Pub(RDP I)54-2 dt. 11-54~~

Subject:- C.Ps. S.Kanara Area. Block I.
Construction of a Primary Health Centre at Bajpe - Additional expenditure - Sanctioned

Read:- 1) G.O.Ms 1405 Pub.(C) dt 27-5-53
2) From the PEO. Mangalore ref. C.No 1625/54-C dt 22-10-54

Order

An expenditure not exceeding Rs 13650/- was sanctioned in the G.O. cited, to meet half the cost of Constructing a primary Health Centre at Bajpe. In actual execution the cost of the sub.works of the Health Centre has varied from the estimate, but the total cost of Rs 27300/- remains unaltered. The actual cost of Constructing a well is now Rs 6600/- against the estimated cost of Rs ~~220~~ 4400/-. The beneficiaries are agreeable to meet half the cost of all other works, but plead inability to meet the half the cost of the excess over the actual cost of the work well. It is therefore agreed to meet half the cost of all items of work except the excess cost on the well which will be fully borne from C.P. funds. The total expenditure thus required is Rs 14750/- Sanction is now accorded to a further expenditure not exceeding Rs 1100/- (Rupees One thousand and one hundred only) over and above the sum of Rs 13650/- sanctioned by the G.O. cited.

2. The expenditure should be debited to "6 a B. C.D. Projects - f. Health and rural Sanitation 1. Works".

3. The PEO. Mangalore is requested to see that the works are completed early and that the Completion report is submitted in due Course.

25/11/54

6.11.54

CENTRAL [illegible]
1.
Rao
Date 25/11/1954. Despatcher's Initials.

To
The PEO. Mangalore
The AG - through Fin. Dept
Copy to The Secy. CPA. Regal Bldgs. N. Delhi
Pub RDP VII, VIII & Tech.

~~RD C.B. 6 months~~

Pub (RDP. V)

(C No. 81301/54)

Sub:- Cls- S. Kanara Area- Block I- Health & Sanitation- Construction of a Primary Health Centre at Bajpe- Construction of a well. Payment for extra work done-

p1 c/f
p2 c/f
pp 3-8 c/f
p 9 c/f

Ref:- 1) From Sri Bhaskar Rai letter dt 12-6-54
2) Ground as Endt No. 81301 Agri (2) 54-1 dt 23-6-54
3) From the PEO. Mangalore ref. C No ~~1625/54~~ C 206/54 dated ~~18~~ 7-54. & subsequent letter No 1625/54 dt 27-7-54.

Please see the letter from the PEO. Mangalore at p9 c/f. This is with reference to the work of Constructing a Primary Health Centre at Bajpe. The work was sanctioned in G.O.Ms. 1405 Pub (CP) dated 27-5-53. for an expenditure of Rs 13650/- out of an estimated cost of Rs 27300, on a basis of half Contribution. The estimate includes a subwork for the Construction of a well 42 feet deep at a cost of Rs 4400/-. The PEO in his letter C. No 2625/53 dated 3-12-53, reported that the well has to be dug for a depth of 57 feet so as to have enough water and his proposal to dig the well to this depth, was approved. The Govt memo No 27027 Agri CP.(consit) 53-3 dt 11-12-53 ~~thereon~~ he was also asked to Submit a workslip or revised estimate, in case the total Cost of the whole scheme exceeds the original estimate for Rs 27300/-.

Subsequently Sri Bhaskar Rai, on behalf of the beneficiaries represented that as the contributions collected so far were just sufficient to carry out the works as per the original estimates and that the extra cost involved in taking the digging of the well from 42 ft to 57 ft. may be met entirely from CP. funds. This letter was forwarded to the PEO. ~~was~~ for Remarks. The PEO in his letter dated 18-7-54 reported that he could not personally contact the Hospital Committee, but

recommended that the extra cost involved in digging the well be met entirely from C.P. funds. He also expected to call a meeting of the Hospital Committee on 25-7-54 to ascertain its views and promised to submit a further report after the meeting

In his letter at p9 c/f, the PEO reports that the Hospital Committee expresses its inability to raise any more funds and wanted full payment for the extra work done on the well. The Committee also has resolved to take up and complete the remaining items of work like latrine, gate way, approach roads and dwelling at 50%. of cost, as soon as orders of Govt. in the matter of paying the extra work done on the well were received In the circumstances the following points ~~may be considered before orders are may be passed~~ arise for consideration.

1) The sanction to an expenditure of Rs 13650/- was accorded on the basis of half Contribution and as such any extra work ~~sanctioned~~ contingent on the work will have to be borne equally by Govt and the beneficiaries

2) The draft hand book fixes the building grant for a primary health centre at Rs 15000/- and similar provision has been made in the approved overall programme also. But there may not be any objection to exceed this limit slightly. The PEO reports that the ultimate expenditure from CP funds is not likely to exceed Rs 15,790 But this is ~~not possible~~ susceptible of check only, if the PEO furnishes a revised estimate bringing out the items of work already completed and yet to be done. This may ~~have to be called for~~ before any definite orders ~~are to be passed~~ decision is taken in the matter. Govt.

3) Some more sub works like latrine, gateway, roads etc

This tendency is on the increase all over the Dist 28.8.54

P1 c/f

A

remain to be taken up, but the Committee has resolved to take up the work only after orders are passed with regard to payment for ~~the well / its work~~ extra work already done. It appears There is no certainty that the Committee will take up these works. The Committee may therefore be asked to commit themselves clearly as to the extent to which they are prepared to meet the cost on the work. So that the balance amount required may be met from C.P. funds.

For orders whether the PEO may be asked to furnish the information as at A on p 2 ante and B above

DS
25.8.54
SD
26/8/54

26/8/84

yes, within ten days

DS
28.8.54

A draft memo is put up for approval

DS
6.9.54
SD
6/9/54

7/9/84

[illegible] as memo. No. 81301 RDP 2/54-28.9.54

I discussed this with the Committee during my recent camp.

The Committee is prepared to meet the cost of the P.H. centre & its appurtenances except the well. In the case of the well, the cost has increased owing to rock being encountered. The Committee desires that its obligation re the well be limited to ½ the original estimated cost. This may be agreed to. PEO will be sending a report. DS 28.9.54

[From the P.E.O. Mangalore Ref. No W 25/54-C dt 22.10.

Please see the letter from the PEO. Mangalore at p 13 cf. The total cost of works actually carried out and of the works to be done is only Rs 27300/-, the same as that of the original estimate. This ~~state~~ is due to the savings on sub-works like the dispensary, Sanitary works & road work, watching the excess on the well, ward of six beds and the Kitchen block., as may be seen from the Comparative statement of differences on pages 21 to 29 cf. The PEO has also reported in his letter at p 13 cf that even if the beneficiaries share the extra cost of the well, their Contribution will only be Rs 13650/- (at half the actual total cost of Rs 27300) which is their originally contemplated share. But in view of the fact that the attitude of the beneficiaries is not for Contributing this full amount, the PEO recommends that the full extra cost of the well i.e Rs 2200/- and half the cost of the other items i.e ½[27300 - 2200] or Rs 12550. may be met from C.P. funds. Thus the total requires is Rs 12550+Rs 2200 or Rs 14750/-. The excess sanction required over and above Rs 13650 already sanctioned is Rs 1100/- and this may now be sanctioned.

A draft memo is put up for approval, w.r.t orders on 3 note.

Finance may see before issue

11.54
8/11/54

8/11/54
W 6.11.54

Finance

G.O 1/s 14-5 Pub dt 27.5.53 at (S)

27300
-2200
2 | 25100
12550
27300 - 12550 = 14750

G.O. at (S) p 3/

[The original sanction accorded in Government Memo the Revised sanction may be seen by them]

Pub (RD PI) Deptt.

W.O. 81301/54-3
6.11.54.



Finance (Exp B)

The draft memo below may be accepted

13.11.54 16.11.54

16/11/54 Pub (A D P)

Fin No: 112066-EB-1
22.11.54

ADDITIONAL ASST. SECRETARY TO GOVT. 23 NOV 1954 3261 PUBLIC DEPARTMENT

Pub (A D P) copies

The notes of Fin above may be perused. They have accepted the draft memo below. It may now be issued

24/11 24/11/54

24/11/54

[Issued as G.O.Ms.No. 2316 Pub dt 26.11.54.]
